☐ Urgent	\square Return Receipt Requested \square Sign \square Encrypt \square Mark Subject Restricted \square Expand personal&public
	RE: (Planning Application No. A/SK-CWBS/42) Request for Further Information 08/09/2022 15:09
From: To: Cc:	"tpbpd@pland.gov.hk" <tpbpd@pland.gov.hk></tpbpd@pland.gov.hk>
Sent by: File Ref:	
Dear Sir/Mac	dam
-	ur application No. A/SK-CWBS/42, we would like to have a deferral request for mation submission.
Detail Deferral peri 2 months	od
Reason Preparing a c	detail tree survey report at new electrical poles position
Best Regards	
Sam Chan	
Tel	Circuits F.) Construction Company Limited oup金城營造集團
From: Sent: Tuesday To: tpbpd@pl Cc:	y, 6 September, 2022 11:45 AM land.gov.hk
	Planning Application No. A/SK-CWBS/42) Request for Further Information
Dear Sir/Mac	dam,
We would like	ke to provide more detail about our application:

1. Drawing of proposed pole is attached.

- 2. This application is for low voltage -380V installation related with proposed poles and underground cables
- 3. According to the application form, the proposed electricity installation will connect to a meter box. This meter box position is under another approved planning application No. A/SK-CWBS/36.
- 4. As the existing network demand nearby is not sufficient for new development, new electricity installation is required.
- 5. This is the most efficiency alignment. the proposed routing is the least impact on nature conservation.
- 6. no tree felling is required
- 7. The tree protection zone should be at least 1.5m away from any tree within 250mm Diameter at Breast Height (DBH) or at least 6 times of the DBH of any tree if their DBH exceeds 250mm.
- 8. To protect the trees, tree protection zone fencing would be installed around the agreed perimeter of the Tree Protection Zone (TPZ). Fencing should be sturdy and highly visible to discourage entrance and disturbance of the area within the TPZ. (details referred to the Figure 3 below).
- 9. Moreover, All sections of fencing should be clearly marked with signs stating that the area within is a Tree Protection Zone and that no one is allowed to enter this area except the authorized person (details referred to the Figure 5 below).
- 10. Excavator will be the first choice if access allowed. Otherwise, the excavation work will be processed by hand tools to minimise the potential impacts to existing trees

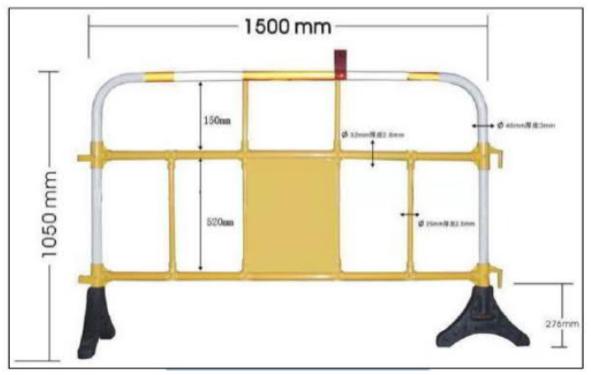


Figure 3. Example of the plastic fencing



Figure 5. Example of TPZ signage

Thank you for your consideration

Best Regards

Sam Chan

Manager
Distribution Circuits
Kum Shing (K.F.) Construction Company Limited
Tel

Kum Shing Group金城營造集團

集團通訊《城訊》KUM SHING NEWS | www.kumshing.com.hk

Disclaimer: This e-mail and its attachment(s) are confidential and may be subject to legal professional privilege and copyright. If you are not the intended addressee, you are hereby notified that any disclosure, usage, retention, dissemination is strictly prohibited. If you have received this mail in error, please contact the sender by returning this email. Thereafter, proceed to delete the entire e-mail from your computer immediately and permanently.
